


# Bond Inspection

Submitted by: mdwaters\_annapolis

Submitted time: Aug 23, 2021, 11:42:58 AM

Location

**Lat: 38.9501 Lon: -76.49617**



Address

**745 annapolis neck**

Date of Inspection

**Aug 23, 2021, 9:09:00 AM**

Type of Project

- **Development**


Site Pictures



site\_pictures-20210823-131151.jpg



site\_pictures-20210823-131526.jpg

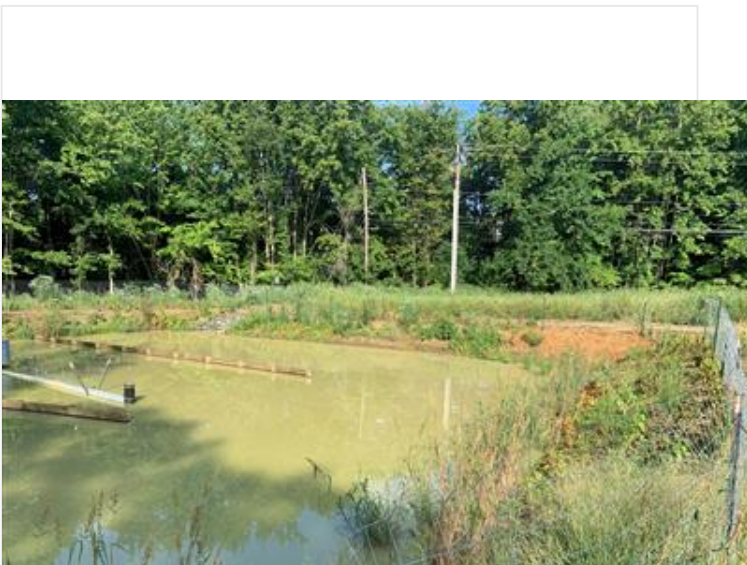



site\_pictures-20210823-131838.jpg



site\_pictures-20210823-131949.jpg



site\_pictures-20210823-132050.jpg



site\_pictures-20210823-132754.jpg





site\_pictures-20210823-132854.jpg



site\_pictures-20210823-133156.jpg



site\_pictures-20210823-133320.jpg



site\_pictures-20210823-133643.jpg



site\_pictures-20210823-134728.jpg



site\_pictures-20210823-134737.jpg



site\_pictures-20210823-134859.jpg

Notes from inspection

**Recommend that millings be added to edge of Annapolis Neck Rd.o**

**Remove road grit and sediment near inlet protection**

**Monitor inflow to sediment trap near front corner.**

**Monitor inflow to sediment trap middle.**

**Build up inflow to sediment trap near townhome area. Also monitor downstream side of sediment trap near the outfall**

**More wood chips at entrance to sewer line work and spots where water is ponding.**

**Monitor inflows to trap at south west corner of townhomes.**
